

On Track



5

At Risk

1

Critical

4

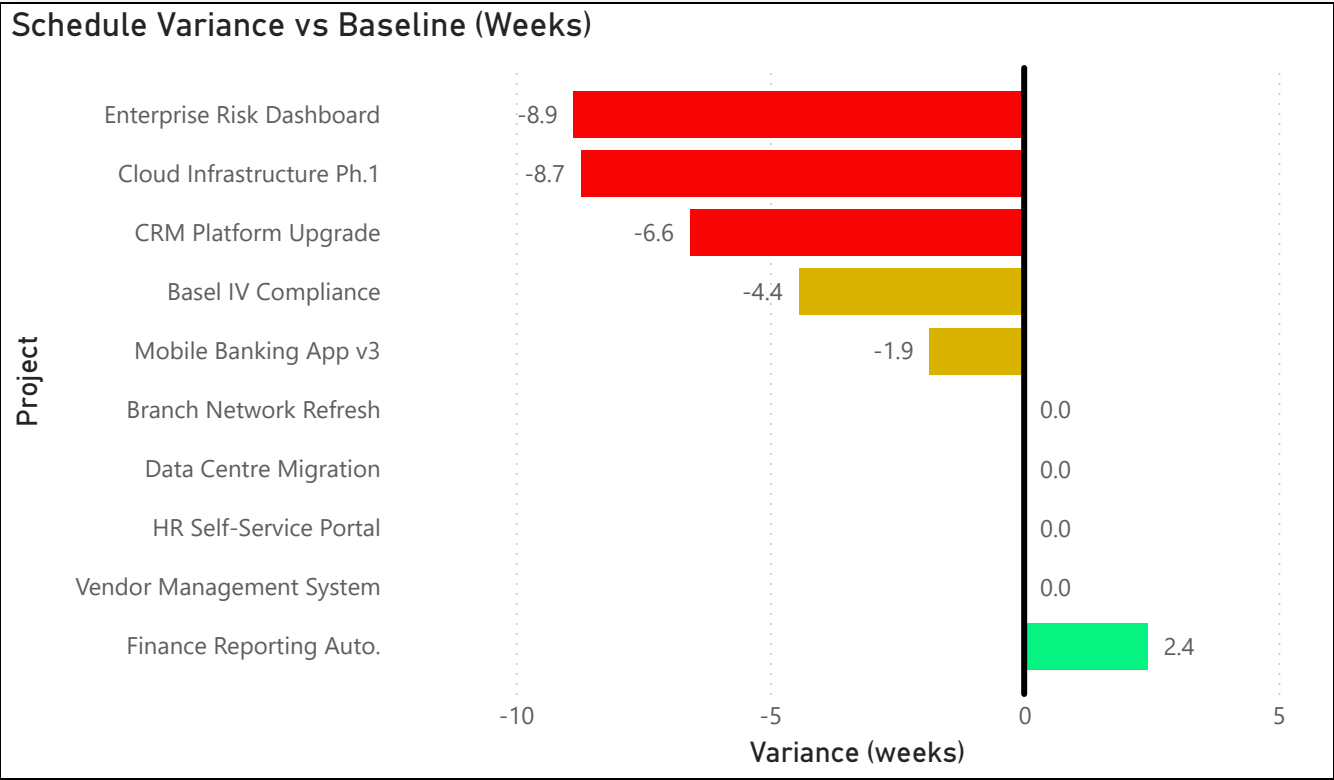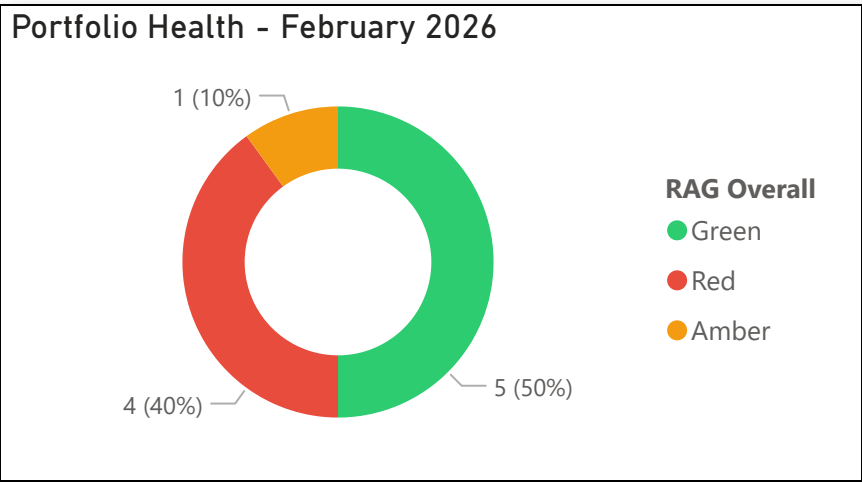


Schedule Risk — Action Required					
Project Name	Forecast End	Variance Wks	Sponsor	Notes	
Enterprise Risk Dashboard	2026-08-31	-8.86	CRO	RED - 9 wks late, SA overload	
Cloud Infrastructure Ph.1	2027-10-15	-8.71	CTO	Under Review - \$100K risk	
CRM Platform Upgrade	2027-04-30	-6.57	CRO	Under Review - no baseline dates yet	
Basel IV Compliance	2026-08-31	-4.43	CFO	AMBER - 4 wks late, 6.7% over	
Mobile Banking App v3	2027-05-13	-1.86	CDO	AMBER - 1.9 wks late, 4.5% over budget	

On-Time Delivery Rate KPI

50%


Budget Performance: Baseline vs Forecast vs Actual (\$K)

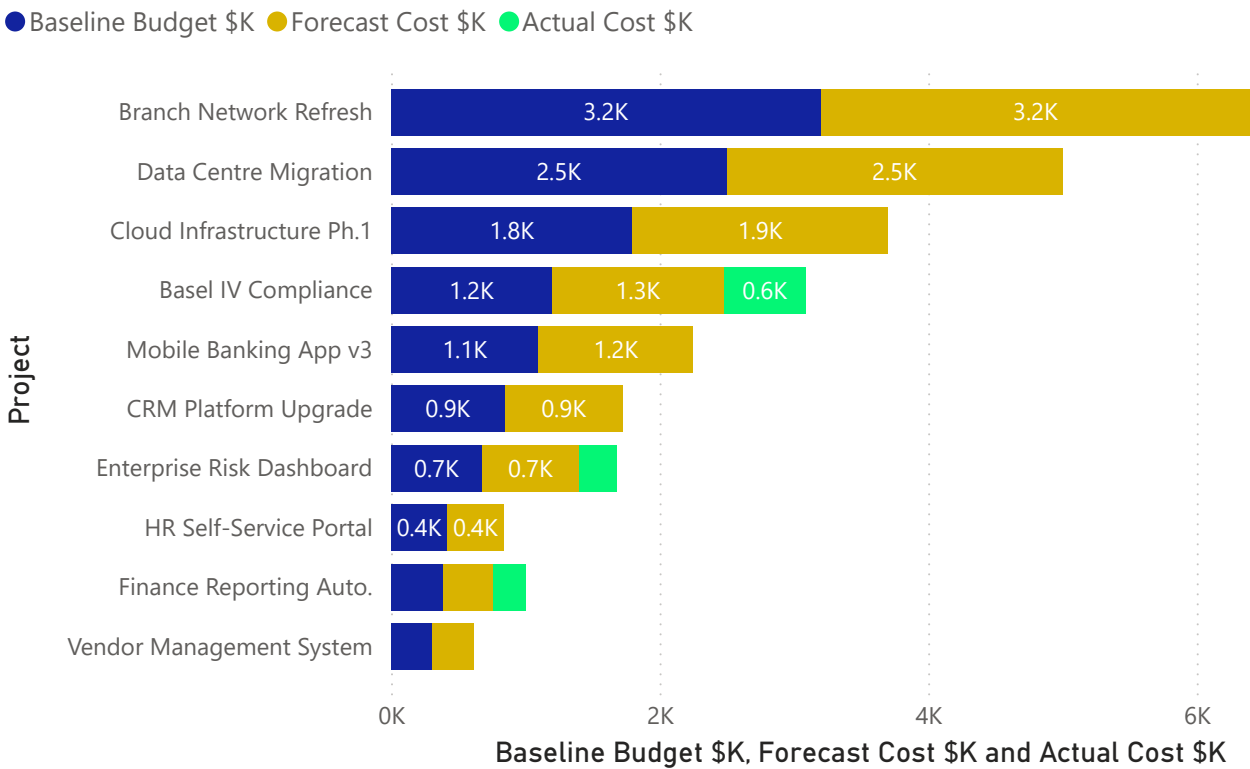

Total Portfolio Forecast Overrun

\$295K

Portfolio Total: Baseline vs Forecast at Completion (\$K)

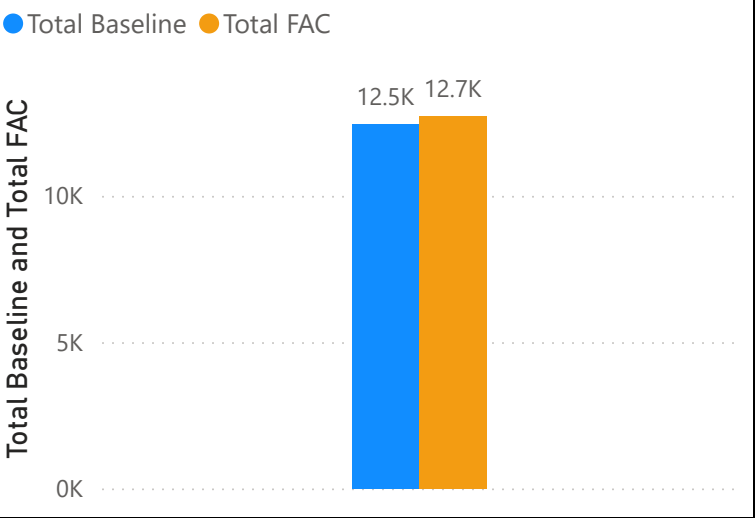

Projects at Financial Risk

Project	Baseline Budget \$K	Forecast \$K	Variance \$K	Variance %	RAG Cost
Basel IV Compliance	1200	1280	-80	-6.67	Amber
Enterprise Risk Dashboard	680	720	-40	-5.88	Amber
Cloud Infrastructure Ph.1	1800	1900	-100	-5.56	Amber
Mobile Banking App v3	1100	1150	-50	-4.55	Amber
CRM Platform Upgrade	850	875	-25	-2.94	Amber
Total	5630	5925	-295	-25.59	

Portfolio Overrun

▲ Overrun: +280K

Open Escalations — PMO Action Required

Project Name	Escalation Type	Description	Days Open	Owner	Escalated to SteerCo
Branch Network Refresh	Risk	Branch Refresh On Hold. Vendor contracts auto-trigger Mar 22 if no scope decision.	27	COO	Yes
Enterprise Risk Dashboard	Risk	SA Wei L. at 142% utilisation across 3 projects — Enterprise Risk Dashboard 9 weeks behind	25	CTO	Yes
Cloud Infrastructure Ph.1	Risk	Cloud Infrastructure SA unavailable until Sep-26. Planned May start at risk.	23	CTO	Yes
Basel IV Compliance	Issue	Basel IV testing backlog 3 weeks. OSFI deadline Apr 30 immovable. Contract BA approval needed.	18	CRO	Yes
CRM Platform Upgrade	Overdue Update	CRM Upgrade PM has not submitted February update. Dashboard cannot publish.	11	PM: TBC	No
Finance Reporting Auto.	Decision	Finance Reporting Auto testing 2 weeks early. Sponsor requesting Apr 30 go-live vs May 31. IT Ops sign-off needed.	8	CFO / IT Ops	No
Total			112		

Decisions Required — SteerCo Action Needed

Decision Item	Options	Owner	Deadline	Consequence if Delayed
Resolve SA resource conflict on Enterprise Risk Dashboard	Dedicate Wei L. / Hire contract SA / Replan timeline	CTO	2026-03-22	P005 stays Red — P010 start delayed to Sep-26
Branch Refresh scope decision — proceed, pause, or cancel	Proceed / Pause / Cancel	COO	2026-03-15	Vendor contracts auto-trigger \$3.2M commitment on Mar 22
Approve contract BA hire for Basel IV testing backlog	Approve hire / Redeploy internal / Accept delay	CRO + CFO	2026-03-08	OSFI deadline Apr 30 missed — regulatory penalty risk


Overdue Updates

10

Overdue Escalations

6

Escalation Summary

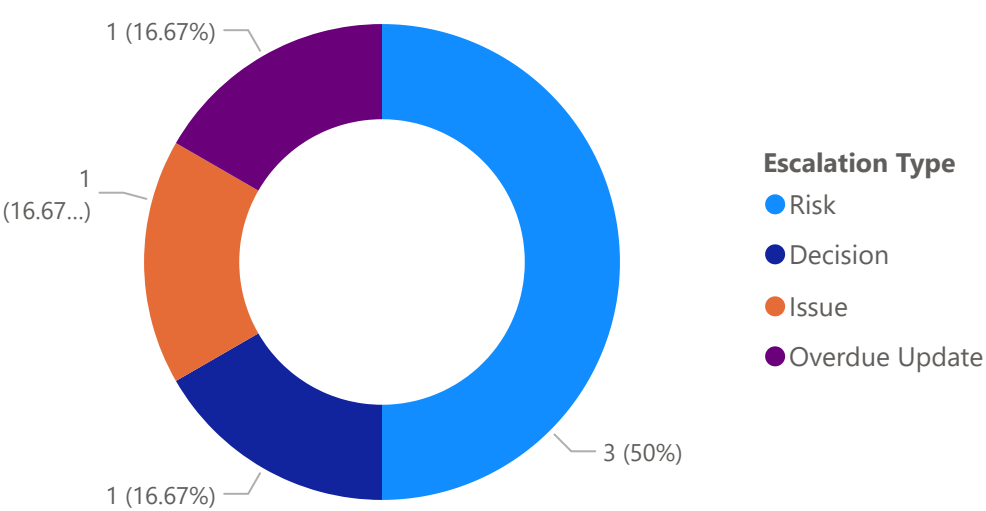

Max Utilization

142%

Total Bench Hours

87.60


Roles at 100%+ Utilization

2

Role Demanded

All

Resource Demand vs Capacity by Role (hrs/week)

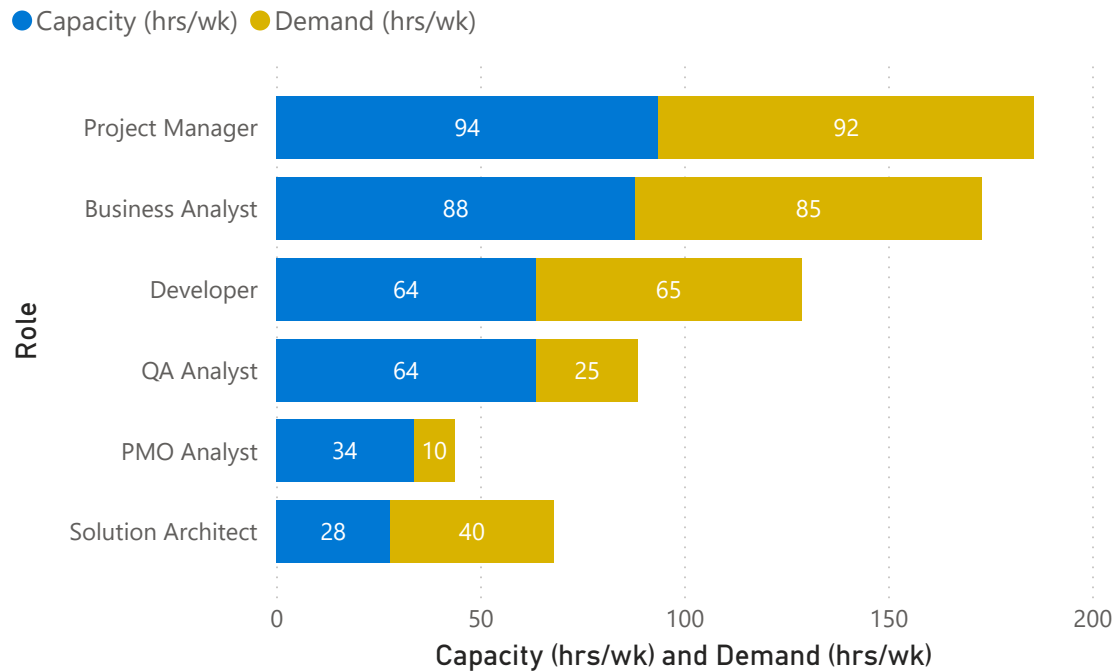

Overload Heatmap Matrix

Role Demanded	January	February	March	April	July	Total
Business Analyst	65	20				85
Developer		30		35		65
PMO Analyst	10					10
Project Manager	80		12			92
Solution Architect	40				20	60
Total	195	50	12	35	20	312

Projects Affected by Constrained Roles

Project Name	Role Demanded	Hrs/Week	Start Month	End Month	Status
Branch Network Refresh	Solution Architect	15	January 2026	April 2026	Confirmed
Cloud Infrastructure Ph.1	Solution Architect	20	July 2026	December 2026	Forecast
Data Centre Migration	Solution Architect	25	January 2026	June 2026	Confirmed
Total		60			
